

MEMORANDUM

DATE: November 19, 2021


TO: Mary Springer
Karla Tacy
Terrejo Arbo

FROM: Eric Kamps, EIT
Daniel Dombos, PE

RE: Michigan Avenue Reconstruction Project Update
MDOT Project #: 80000-207882/210862

Current Progress

Davis Construction and their subcontractors worked this week along Michigan Ave. The concrete subcontractor was on site this week to place concrete forms and grade the remaining sidewalk and sidewalk ramps in preparation for the placement of concrete. Placement of concrete began late in the week on the remaining areas along Michigan Ave and Kalamazoo Street. Along with the concrete subcontractor, the electrical subcontractor was on site this week to continue work on preparing the site for the placement of the new light poles by placing the wire for the new lighting system. Davis Construction had their irrigation workers on site this week to continue to work on completing the irrigation system in the 200 and 300 blocks of Michigan Ave.

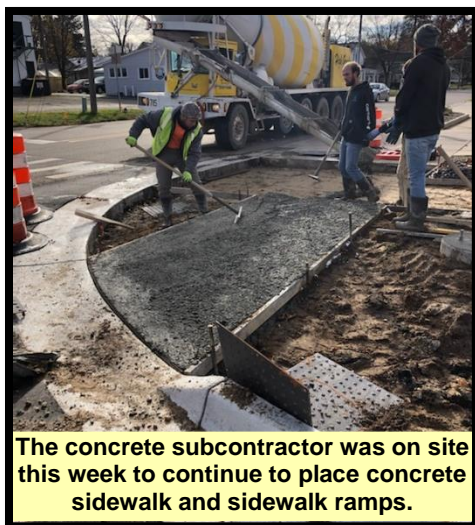

Next Week's Schedule

Davis Construction will continue to work with their subcontractors next week. The electrical subcontractor will be on site to begin to place the new light poles. The irrigation crew will also be on site to continue placing the irrigation system throughout the week. The concrete crews will also be working with Davis Construction to work on completing the sidewalk and sidewalk ramps, as well as preparing and placing driveways along Michigan Ave. With the final paving being complete and the pavement marking being placed, the roadway is fully opened to allow traffic in every direction. The edges of the roadway in some areas will remain closed to allow for work to continue as needed to complete the remaining work on the project.

If you have any project questions or concerns, please contact Eric Kamps with Abonmarche Consultants at ekamps@abonmarche.com or (269) 926-4556.
